



	<b>Location:</b> Gamuda Gardens 2 Road, Gamuda Gardens, Hoang Mai District, Hanoi
	<b>Total land area:</b> 2.3 ha
	<b>NOS (full phase):</b> Appx. 2,000 students
	<b>Phase 2 components:</b> - Block 2 for Kindergarten, Primary and Junior High School students (GFA: 4,084 sqm) - Swimming pool (600 sqm); Kindergarten pool & playground - Other supporting facilities
	<b>Phase 2 timeline:</b> - December 2017: Started construction - August 2018: Operation commencement
	<b>Construction contractor:</b> Viteccons Investment and Construction JSC
	<b>Site supervisor:</b> Consultant and Inspection Joint Stock Company of Construction Technology and Equipment - CONINCO

### Construction update

#### Block 2:

- ✓ Brick work & plastering work done. Started painting
- ✓ Installation of roof done
- ✓ Installation of doors, windows, glasses in progress




**Block 2 frontage**



**Internal plastering work at Block 2**



**Installation of windows**

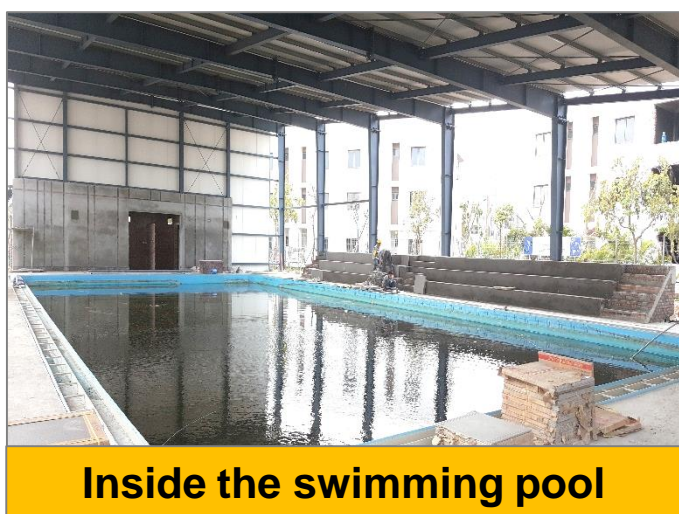

**Inside the swimming pool**



**Pool for Kindergarten students**

#### Swimming pool area:

- ✓ Installation of pool shell, pool roof done
- ✓ Brick work for auxiliary house done



**Swimming pool area**

#### Upcoming plan:

- ✓ By Mid June: complete construction work
- ✓ July: install Furniture, IT and other equipment
- ✓ 6<sup>th</sup> Aug 2018: start new academic year 2018 - 2019
